



KWARA STATE GOVERNMENT

**PROJECT: THE COMPLETION OF CONSTRUCTION OF
INFORMATION, COMMUNICATION TECHNOLOGY HUB FOR
KWARA STATE GOVERNMENT, ILORIN**



WEEKLY REPORT

DATE REPORTED: 29TH MARCH, 2024



Geniserve Limited:

34A, Oduduwa Way, GRA Ikeja, Lagos.

Tel: +234 1 2904865, 0808 410 7442, 0909 239 5277, 0909 039 0167

info@geniserveng.com, www.geniserveng.com

OUTLINE

- ▶ List of completed tasks
- ▶ List of tasks yet to start
- ▶ Ongoing Tasks (Under Construction)
- ▶ Progress Statistics
- ▶ Work Progress Images
- ▶ Challenges and Recommendations

LIST OF COMPLETED TASKS

INTERNAL WORKS

S/N	DESCRIPTION	RESPONSIBLE MANAGER
1	Dressing of windows (First and second floor)	MC&T
2.	POP Screeding for the internal walls	MC&T

EXTERNAL WORKS

S/N	DESCRIPTION	RESPONSIBLE MANAGER
1	Hacking and Plastering of walls	MC&T
2	Replastering of isolated columns	MC&T
3	Demolition of old soak away and construction of new soak away	MC&T
4	Construction of circular flowerpot	MC&T
5	Fence works	MC&T
6	POP screeding for external walls	MC&T
7	Roof coating	MC&T
8	POP Screeding for the Generator House and Security House	MC&T
9	Construction of storage for Space Finish Ltd.	MC&T
10	Roofing of the Generator House	MC&T

LIST OF TASKS YET TO START


- ▶ Central air conditioning
- ▶ Elevators
- ▶ Solar Power
- ▶ Screen
- ▶ Granite Floor Tiles
- ▶ Extension of Control Room (Combining cloakroom and control unit)
- ▶ New concrete columns required at the Didactic Room
- ▶ Space Finishing
- ▶ Electrical works

ONGOING TASKS (UNDER CONSTRUCTION)

S/N	TASKS	RESPONSIBLE MANAGER	TIMELINE	% WORKDONE
1	Electrical Piping works	MC&T	-	90
2	Additional toilets	MC&T	-	89
3	Water tank fabrication	MC&T	-	15
4	Internal Drainage works	MC&T	-	98
5	Cutting and filling of surrounding levels	MC&T	-	72
6	Horticulture	MC&T	-	46
8	External Kerbs	MC&T	-	80
9	Floor screeding to receive Tilling	MC&T	-	69
10	Plumbing works	MC&T	-	58
11	Curtain wall glass installation	MC&T	-	95
12	Construction of overhead water tank, water treatment and stanchion structure	MC&T	-	20
13	Construction of security lights poles along the perimeter fence	MC&T	-	85
14	External drainage works	MC&T	-	66

PROGRESS STATISTICS

WORK COMPLETION PERCENTAGE (%)

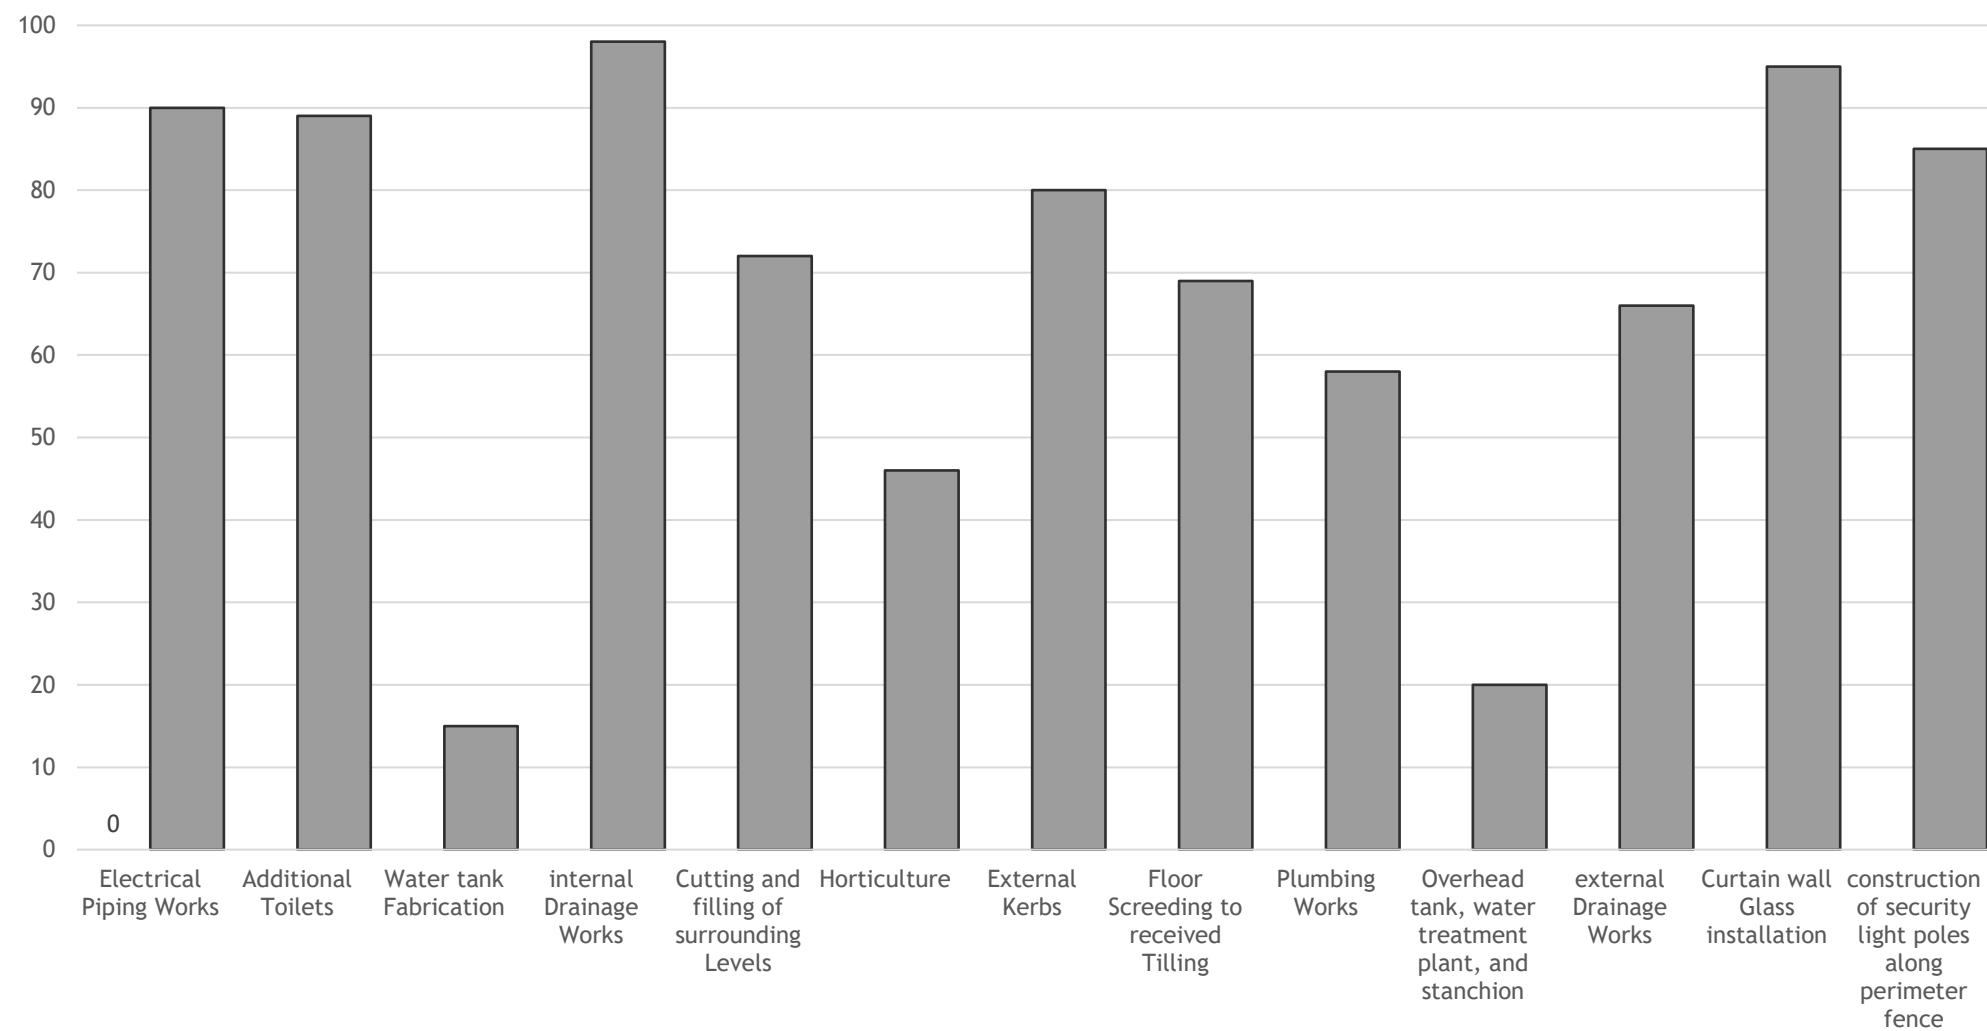

DESIGN WORKS

S/N	DESCRIPTION	STATUS
1	As-built design of existing elevator and proposed panoramic elevator	Done
2	Structural analysis and design of areas where additional columns are needed (Didactic Room and Multipurpose Room)	Done
3	Structural design of mezzanine floors at Conference Hall, Multipurpose Hall, floor extension for the general and alternative workspace	Done
4.	Architectural redesigning of roof drainage at the exterior side	In progress

OTHER INSTALLATIONS

➤ Air Conditioning:

- ▶ The option of a cassette unit with Samsung Nig. has been reviewed, and we are confident with our choice in terms of costs and time.
- ❓ We also have a quote and design for the VRF System from a vendor named VACC.
- ▶ While we are recommending Samsung for the reason of price competitiveness, we will still require Samsung to give us a CFD analysis of a guarantee that the system will perform optimally as designed.
- ▶ Technical evaluations on all quotes have been accomplished. We await finalization by IHS on the preferred vendor based on our evaluations.

➤ Solar Systems:

- ▶ Technical and financial evaluations of designs and quotes from three vendors have been finalized, and a recommendation on the best option has been proffered.
- ▶ We await finalization of the quotes by IHS.

➤ LCD Screen:

- ▶ Technical and financial evaluations from two vendors have been concluded, and we have forwarded our appraisalment from both parties for finalization.

➤ Elevator:

- ▶ Geniserve has performed technical evaluations and cost analysis of quotes from three vendors. Recommendations have been sent to IHS for their final decision on their preferred vendor for the delivery and installation of the elevator.

PROGRESS PHOTOGRAPHS




External Drainage: Concrete Blinding, Block setting and weak concrete hollow filling works in progress

PROGRESS PHOTOGRAPHS



Roofing of the Generator House completed

PROGRESS PHOTOGRAPHS

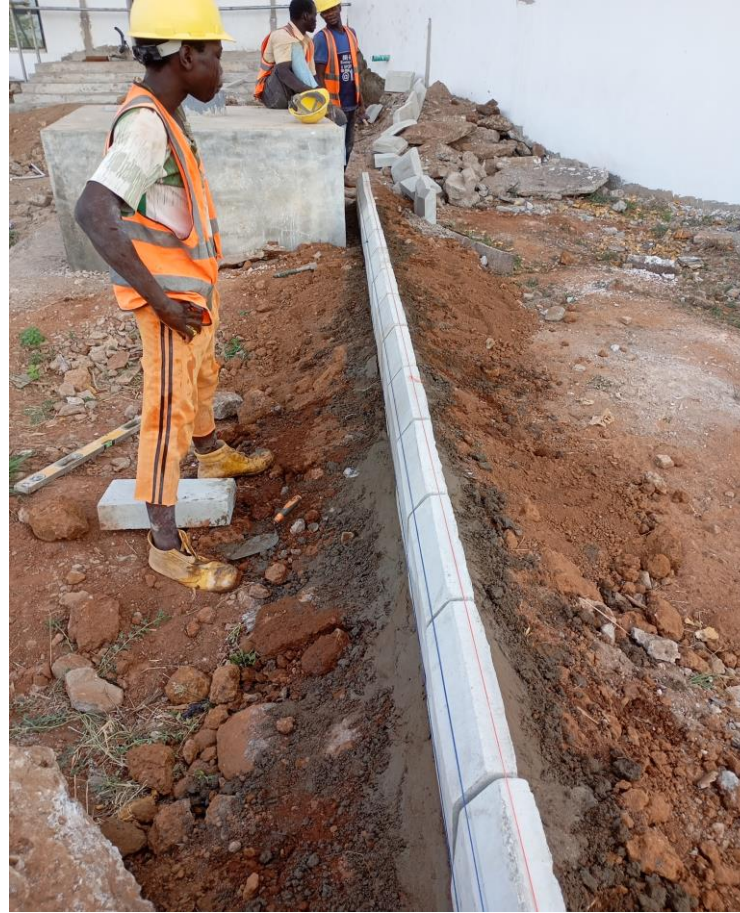

Setting of Precast kerbs at the back of the main building in progress

PROGRESS PHOTOGRAPHS



Setting out of column base for the floor slab extension

PROGRESS PHOTOGRAPHS



Compound Level in progress

PROGRESS PHOTOGRAPHS



Installation of curtain wall glass in progress

PROGRESS PHOTOGRAPHS



Plumbing works in progress

CHALLENGES AND RECOMMENDATIONS

Challenges:

- ▶ There is no PIP on the project for us to integrate all other vendors PIP with, in order to monitor the timeline for project completion.

Recommendation

- ▶ We advise that the Implementing Vendor should provide the Project Manager (Geniserve Ltd) with a PIP for proper project management and also to mitigate against any likely delays on the project.

DELIVERABLES

This Week

S/N	ACTION PLAN	RESPONSIBLE PARTY	CURRENT STATUS	EXPECTATIONS
1	Finalizing the preferred quotes on cooling system by IHS	SAMSUNG & VACC		
2	Completion of security lights along the perimeter fence	MC&T	85%	100%
3	External Drainage Works	MC&T	66%	68%
4	Partitioning of additional Toilets in the main building	MC&T	89%	100%
5	Submission of LCD screen design and quote	Samsung	Done	Done
6	Finalizing the most preferred quote on elevator choice by IHS.	Bethel V.O, Kresta L. Ltd, & E LAVI		
7	Cutting and filling of surrounding levels	MC&T	72%	78%

DELIVERABLES

Projections for Next Week

S/N	ACTION PLAN	RESPONSIBLE PARTY	CURRENT STATUS	EXPECTED STATUS BEFORE NEXT WEEK FRIDAY
1	Finalizing the preferred quotes on cooling system by IHS	SAMSUNG & VACC		
2	Completion of security lights along the perimeter fence	MC&T	85%	100%
3	External Drainage Works	MC&T	66%	75%
4	Submission of LCD screen design and quote	Samsung		
5	Finalizing the most preferred quote on elevators by IHS.	Bethel V.O, Kresta L. Ltd, & E LAVI		
6	Cutting and filling of surrounding levels	MC&T	69%	78%
7	Begin the Extension of first floor concrete slab at conference room	MC&T		
8	Construction of Mezzanine floor slab & extensions	MC&T	3%	10%

THANK YOU

SPONSORED BY:



CONSULTING PROJECT MANAGER:



Geniserve Limited:

34A, Oduduwa Way, GRA Ikeja, Lagos.

Tel: +234 12904865, 0808 410 7442, 0909 239 5277, 0909 039 0167

info@geniserveng.com, www.geniserveng.com
